






## Appendix A Construction Programme

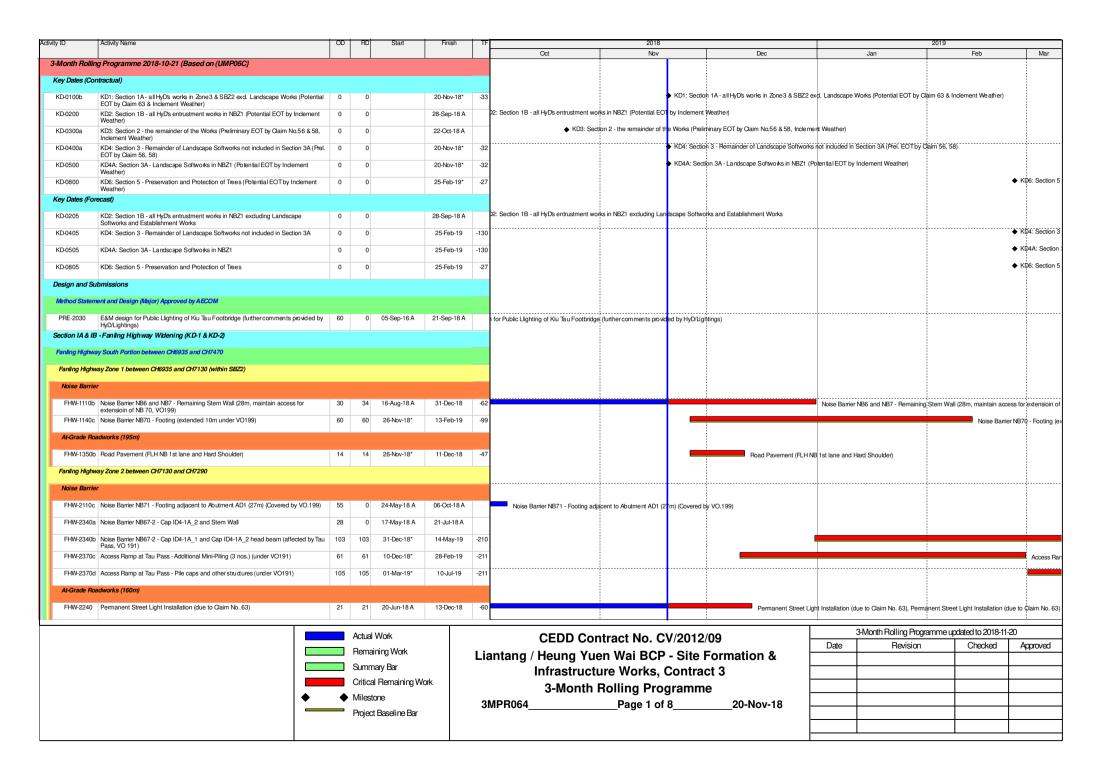


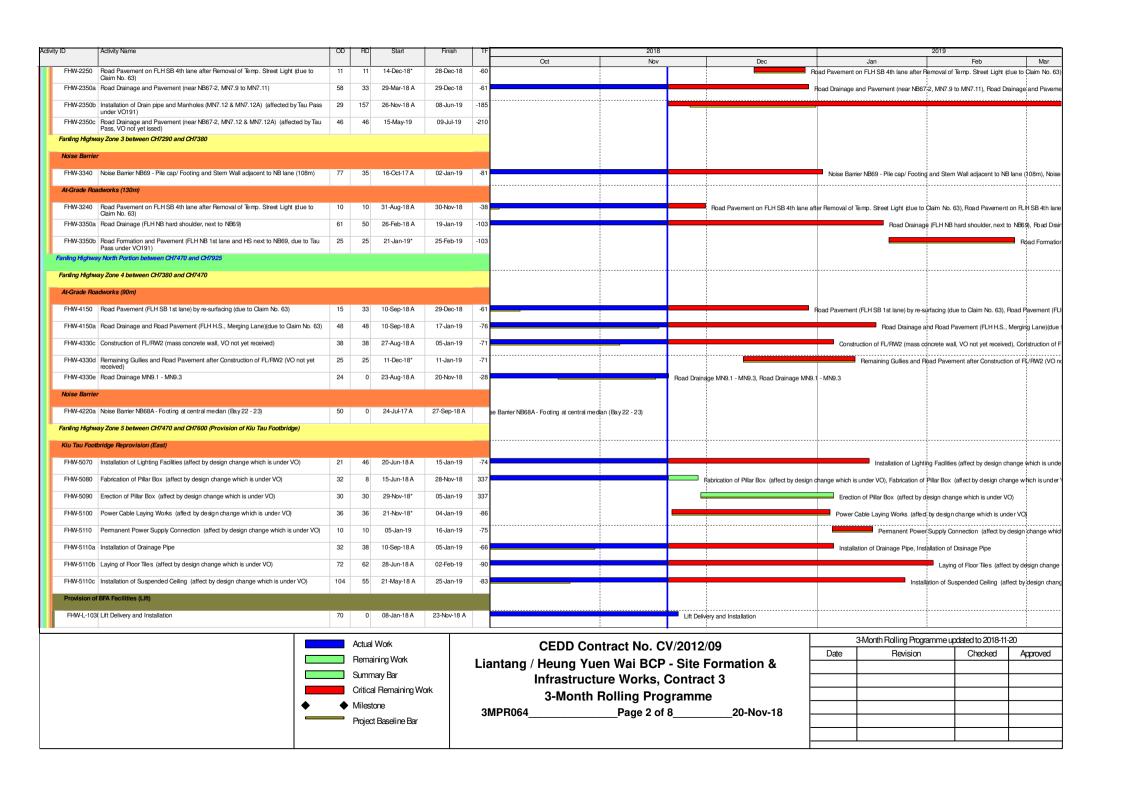


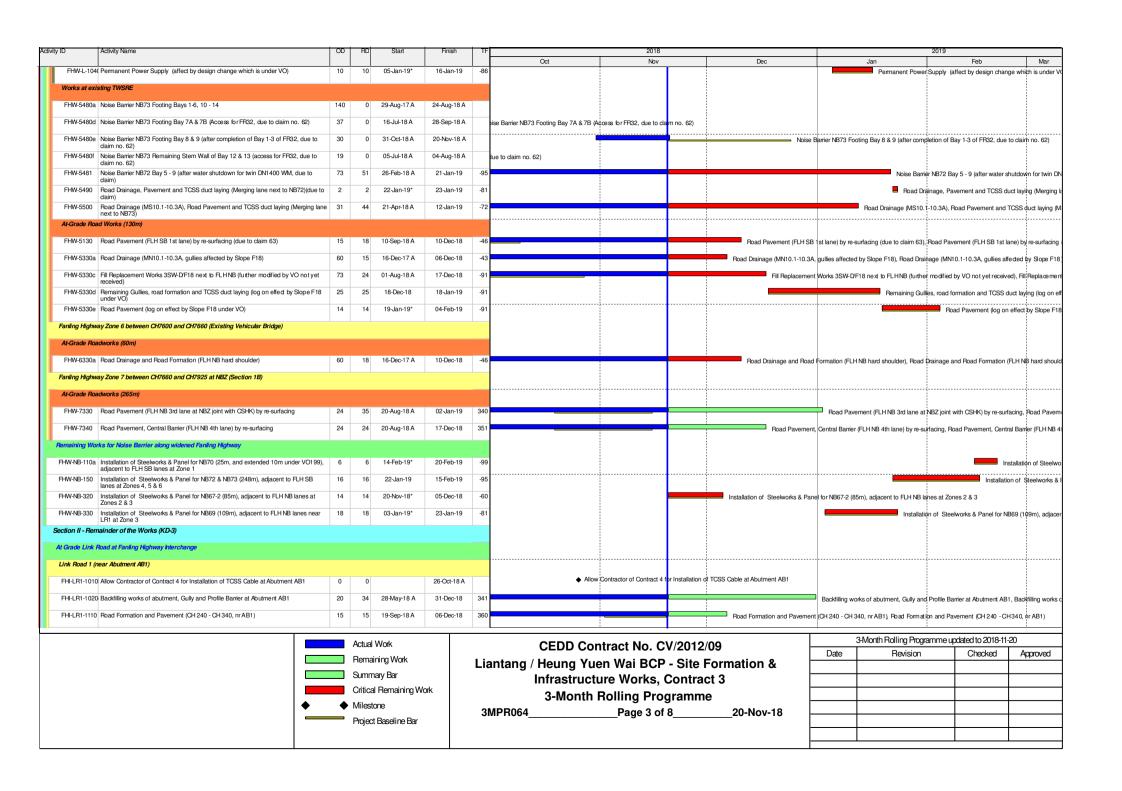

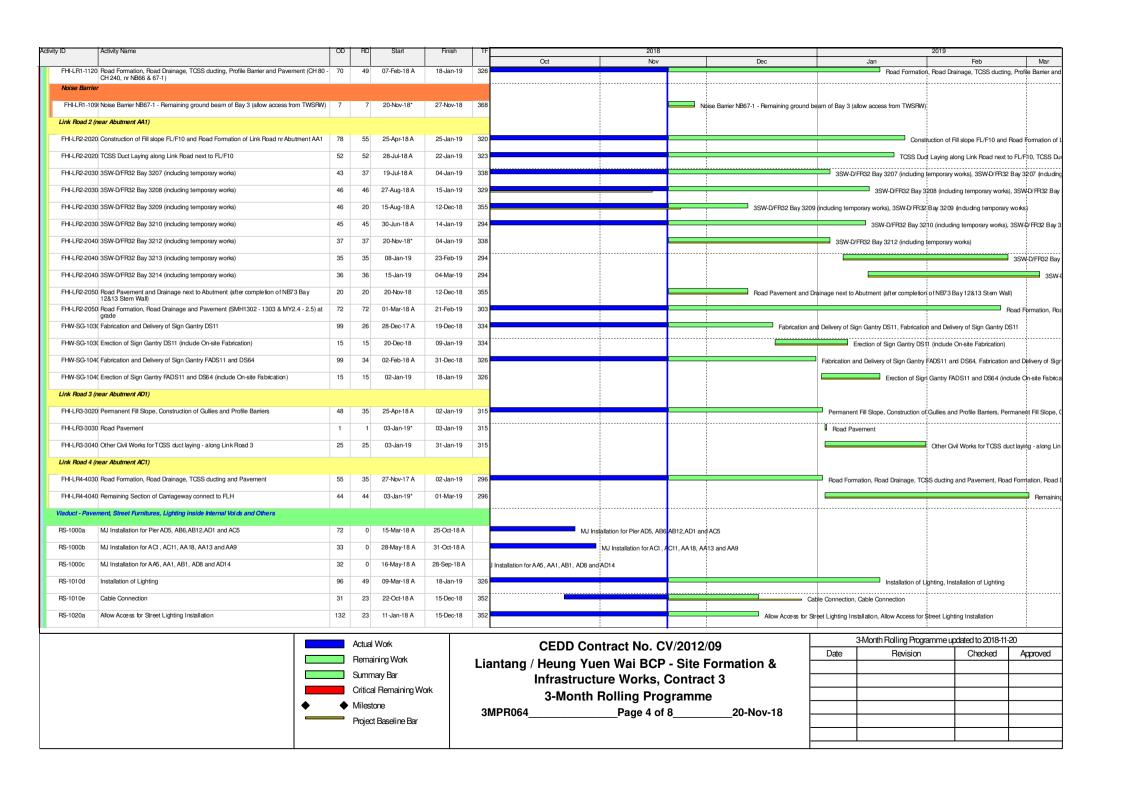

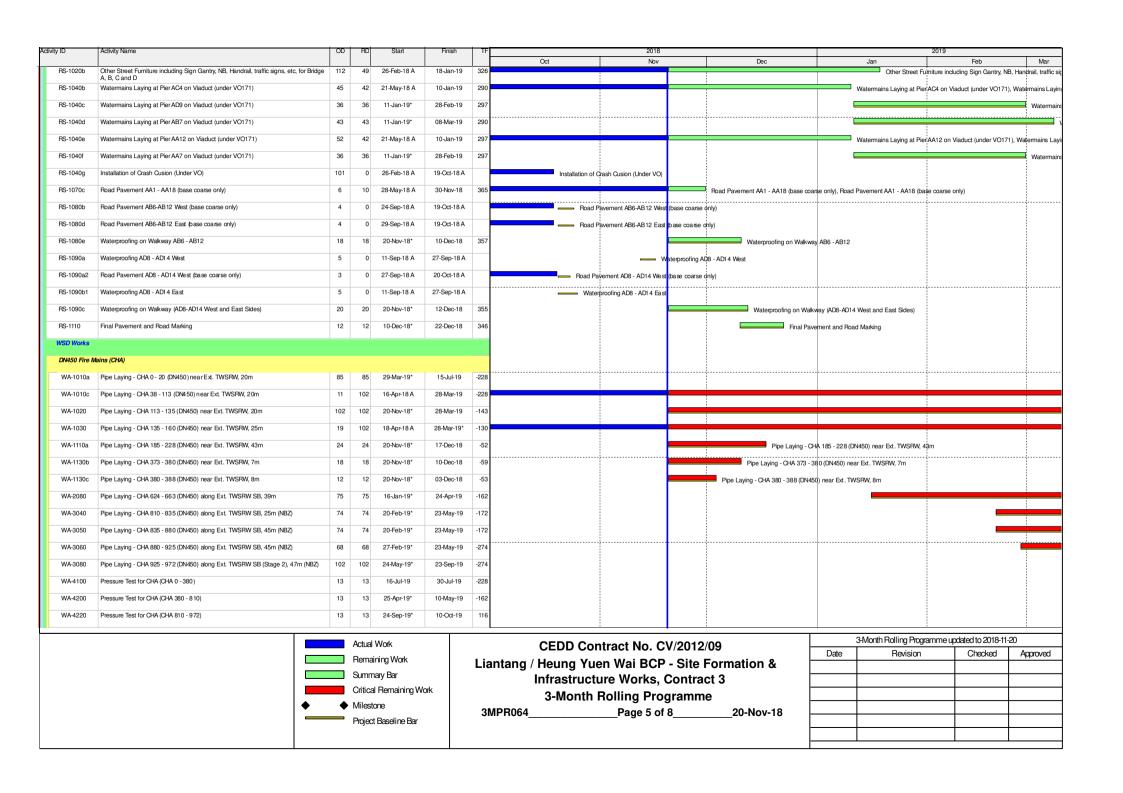

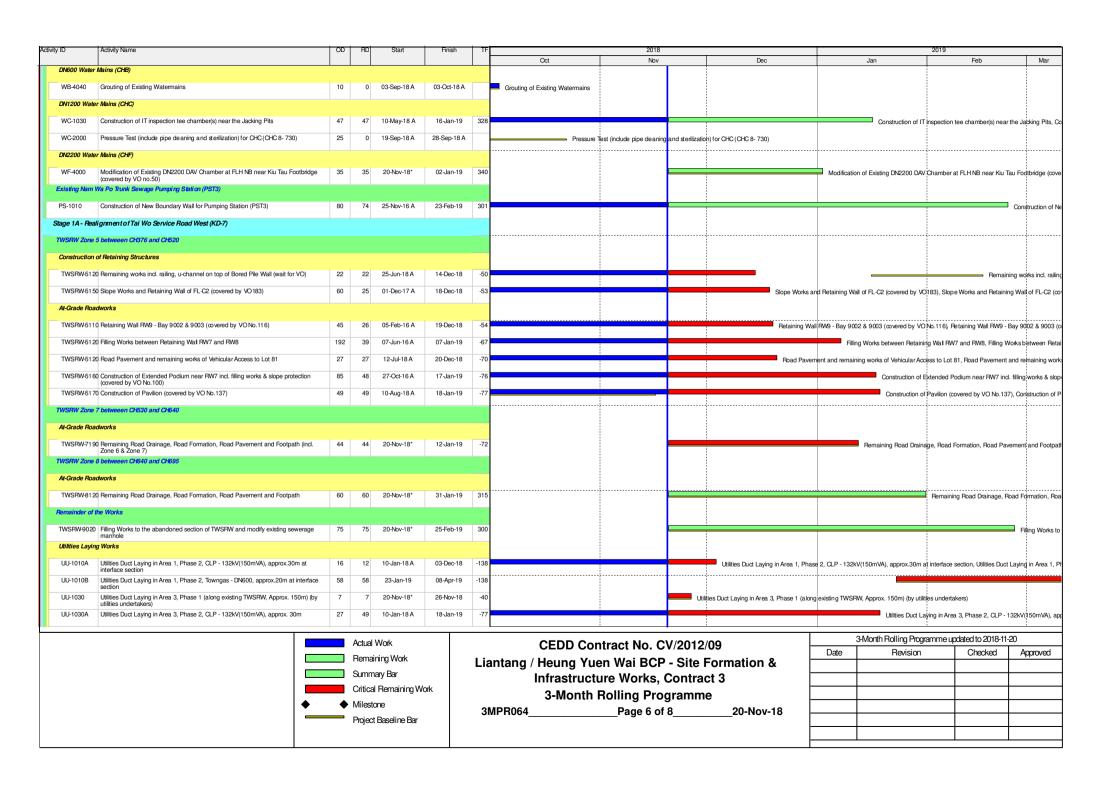

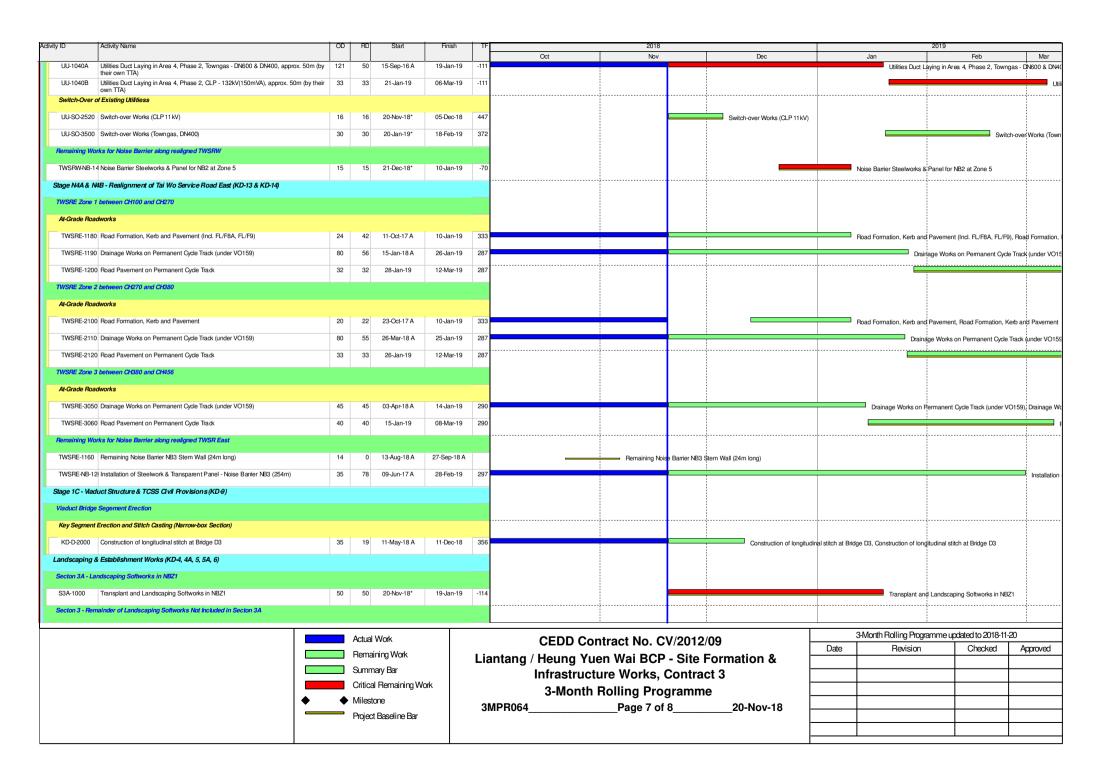

| Activity ID     | Activity Name   | OD                 | RD                           | Start                                 | Finish    | TF   | 2018   |         |                      | 2019                          |                                     |
|-----------------|---|--------------------|------------------------------|---------------------------------------|-----------|------|--|---------|----------------------|-------------------------------|-------------------------------------|
|                 |   |                    |                              |                                       |           |      | Oct Nov  | Dec     | Jan                  | Feb                           | Mar                                 |
| S3-1000         | Transplant and Landscaping Softworks on At grade Road                   | 131                | 75                           | 26-Mar-18 A                           | 25-Feb-19 | -138 |  |         |                      |                               | Transplant and                      |
| S3-1010         | Transplant and Landscaping Softworks on Viaduct or other remaining area | 48                 | 48                           | 20-Nov-18*                            | 17-Jan-19 | -75  |  |         | Transplant and La    | andscaping Softworks on Vadud | torother nemainin                   |
| Section 4A: Es  | tablishment Works for Landscape Softworks under Section 3A              |                    |                              |                                       |           |      |  |         |                      |                               |                                     |
| S4A-1000        | Establishment Works at NBZ1   | 365                | 365                          | 20-Jan-19                             | 19-Jan-20 | -140 |  |         |                      |                               |                                     |
| Section 4: Esta | ablishment Works for Landscape Softworks under Section 3                |                    |                              |                                       |           |      |  |         |                      |                               |                                     |
| S4-1000         | Establishment Works for Remaining Part of Site                          | 365                | 365                          | 26-Feb-19                             | 25-Feb-20 | -175 |  |         |                      |                               | $\leftarrow$                        |
| Section 5: Pres | servation and Protection of Trees                                       |                    |                              |                                       |           |      |  |         |                      |                               |                                     |
| S5-1000         | Preservation and Protection of Trees                                    | 0                  | 0                            |                                       | 25-Feb-19 | -17  |  |         |                      |                               | <ul> <li>Preservation an</li> </ul> |
|                 |   |                    |                              |                                       |           |      | i i  |         |                      |                               |                                     |
|                 |   |                    |                              |                                       |           |      |  |         | 3.Month Pollim Prove | amme updated to 2018-11-2     | 5                                   |
|                 | •   | \$ ( \dag{\psi} \) | Summa<br>Critical<br>Milesto | ning Work<br>ary Bar<br>Remaining Wor | rk        |      | CEDD Contract No. CV/2012/09 ng / Heung Yuen Wai BCP - Site Forma Infrastructure Works, Contract 3 3-Month Rolling Programme 064 | ation & | ate Revision         | Checked                       | Approved                            |
